

PO Box 930 1470 NE Territorial Road

Phone: 503.266.0798 Fax: 503.266.7238 Canby, OR 97013 www.canbyoregon.gov

Okada America

368 & 372 S Sequoia Parkway October 26, 2021 **Utility Notes**

PUBLIC WORKS DEPARTMENT – SEWER

- 1. Tie into the existing manhole. Everything behind the manhole into the property is
- 2. Contact Daryll Hughes and see if a sampling manhole will be required for the building because of the usage of the existing manhole.

Stormwater

1. Drywell in the cul-de-sac is private.

CANBY FIRE DEPARTMENT

- 1. Access to property is good.
- 2. Private fire line.
- 3. Engineering to work with the Fire Department on placement of fire hydrants.

DIRECTLINK

- 1. We are stubbed out at the end of the cul-de-sac.
- 2. We will need the location for the communication room.

NOTES:

Comments from DirectLink for New Building with D-mark in side:

- The Developer/Owner is required to provide all trenches for placing underground communication facilities from the existing connection point. We will place and provide all materials.
- We will follow the power design as much as possible to minimize trenching; however, a separate trench may be required for communication services.
- If the D-marc is required to be placed in a communication / power room, the requirements are:
 - 1. 2" schedule 40 PVC from the telephone connection point outside, into the Communication / power room with a 36" sweep (minimum).
 - 2. One 4'x8' 3/4" plywood backboard or coated with fire retardant paint.
 - 3. #6 stranded grounds (MGN) connected to approved ground provided at the backboard.
 - 4. One 15 Amp electrical outlet located next to / or on backboard.
- For temporary service (job shack), contact our Customer Care Center to place an order.
- We do not charge development fee.

CANBY UTILITY – WATER


- 1. Need the meter size.
- 2. Requiring an RP backflow device.
- 3. Need to pay all system development charges and meter fees before waterline construction begins.
- 4. If any elevated water piping over 30 ft will require an RP device.
- 5. All cost sheets and as-builts need to be submitted to Canby Utility before final inspection/occupancy.

ELECTRIC

1. There is a possibility of adding a 444 vault.

ADDITIONAL NOTES

- 1. No construction will begin without a signed set of construction plans delivered to all utility providers. If work starts without the signed construction plans, there will be a stop work and it will be at the owner's expense.
- 2. All equipment and private vehicles must remain on work site within the erosion control fencing. If equipment or vehicles are found off-site the project will be stopped and will be at owner's expense.
- 3. All utility easements will be free of any obstructions.
- 4. Follow all erosion control measurement.
- 5. Check with the Planning Department for street lighting of the cul-de-sac, this lighting will be private.

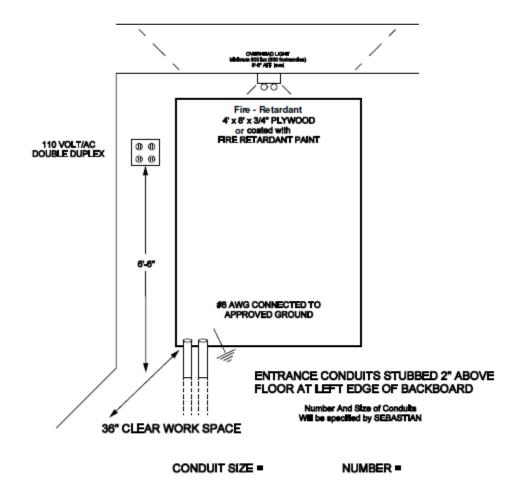

NOTE: Grounding source options are Electrical Power Service Grounding Electrode, Service Grounding Electrode Conductior or Service Panel, UFER, grounding ring, or driven ground rod.
